

**CHARLOTTESVILLE RESIDENCY MONTHLY REPORT**  
**JULY 2005**

**CONSTRUCTION**

*Active Construction Projects*

**Route 649 (Airport Road improvement project) 0649-002-158, C501**

Original completion date: 9/2/2005 Award amount: \$4,820,177  
Estimated completion date: 11/1/2005 Est. completion amount: \$4,855,598

- Traffic is running on the completed new westbound lanes of Rt 649. Contractor is demolishing existing Rt 649 and beginning grade work for proposed eastbound lanes..

**Route 20 (Carter's Bridge replacement project) 0020-002-126, C501, B608**

- Project completed 7/20/05.

**Route 53 (Buck Island Creek bridge replacement project) 0053-002-101, C501, B601**

Original completion date: 11/1/2005 Award amount: \$1,644,187  
Estimated completion date: 11/1/2005 Est. completion amount: \$1,644,187

- Contractor has completed driving steel pilings and placing concrete footers for both the north and south side bridge abutments.

**BP-7A-05 (District wide bridge painting project)**

Original completion date: 10/31/2005 Award amount: \$1,556,670  
Estimated completion date: 10/31/2005 Est. completion amount: \$1,556,670

- Continuing work on Rtes. 690 and 691 bridges over I-64. Beginning work on the I-64 bridge over Rt 781. VDOT is to receive a plan from the contractor for restoring satisfactory progress on this project.

**PM-7B-05 (Asphalt pavement overlay)**

Original completion date: 12/1/2005 Award amount: \$3,699,919.31  
Estimated completion date: 12/1/2005 Est. completion amount: \$3,699,919.31

- Scheduled sections of Rtes. 6 and 53 complete. Paving on Proffit Rd. from Rte. 29 connection to Rte. 20 is proceeding.

**BR-7C-05 (Bridge deck repairs and epoxy overlay)**

Original Completion Date: 11/1/05 Award amount: \$296,055.50  
Estimated Completion Date: 11/1/05 Est. Completion Amount: \$317,055.50

- Contractor completed bridge deck patching on the Rte. 744 bridge over I-64 and the Rte. 722 bridge over Rockfish Creek.

**BB-7A-05 (Shotcrete pipe culvert rehab)**

Original Completion Date: 7/29/05 Award amount: \$ 113,745.04  
Estimated Completion Date: 7/29/05 Est. Completion Amount: \$113,745.04

- All pipe culvert rehab sites scheduled on this project are complete.

**MAINTENANCE WORK COMPLETED**

**Albemarle County**

- Mowed various secondary routes, 80% finished first cycle, 100% finished second cycle Primary.
- Patching operations complete on Rtes. 250, 614, 601, 1315, 866, 743, 671, 665, 1403, 606, 630, 717, 810, 604, 621.
- Ditching operations complete on Rtes. 674, 690, 796.
- Specialty Crew work complete on Route 810 bridge; new concrete paved ditch at Rt 1433 (Carrsbrook) Installed cables and timber deck on Rt 743 bridge.
- Guardrail mowing on Route 20, 627, I-64.
- Rural rustic road putting down base stone Route 640.
- Grading and adding stone on Rts. 673, 674, 829, 668, 643, 672, 667, 697, 736, 824, 633, 634.

### Greene County

- Mowing complete first cycle secondary, second cycle primary.
- Patching operations complete Rts. 810, 604, 721, 626, 603, F981.
- Guardrail mowing on Route 33, 810, 1001, 633, 621, 29.
- Ditch and pipe work Rts. 626, 614, 632, 637.

## PRELIMINARY ENGINEERING

### Albemarle County

- **Route 22 / 250 Intersection Improvements, 0022-002-104, C501**  
On schedule for spring 2008 Construction with ROW acquisition to begin in August 2005.
- **Route 631 McIntire Road, 0631-002-128, C502, B612, B657**  
On schedule for a June 2008 Ad Date with ROW acquisition scheduled to begin in December 2005.
- **Route 691 Jarmans Gap Road, 0691-002-158, C501**  
Has been rescheduled for December 2009 Ad Date. The Public Hearing is rescheduled for Spring 2006.
- **Route 656 Georgetown Road, 0656-002-254, C501**  
Scoping to be scheduled in September. Planned consultant design. CIM planned for Spring 2006.
- **Route 606 Dickerson Road, 0606-002-P75, N501**  
On schedule for a December 2007 Ad Date. The ROW for this gravel road project is only partially available.
- **Route 640 Gilbert Station Road, 0640-002-P78, N501**  
Construction began on June 13, 2005, using State Forces. Projected to be completed in August.

### Greene County

- **Route 627 Bacon Hollow Road, 0627-039-195, C501**  
Project is on schedule for December 2006 Ad Date.

## PLANNING, PERMITS AND LAND DEVELOPMENT

Land Development Items	Total This Month	Total This Fiscal Year
Special Use Permits and Rezoning Application Review	11	93
Site Plan Reviews for new Subdivisions	6	92
New Entrance Plan Reviews	7	107
Total Permits Processed	78	679
Utility Permits Processed	22	177
Inspection of new Subdivision Street conducted	14	101
Inspection of new entrance conducted	85	855
Miles of Street Accepted in the State System	0.28	5.89

**TRAFFIC ENGINEERING**

**Albemarle - Complete June - July**

<b>Route</b>	<b>Location</b>	<b>Received</b>	<b>Issue description</b>	<b>Planned Action</b>
22	Near Cismont	6/22/05	Request for curve road sign, entrance sign	Not recommended
240	Crozet	6/1/05	Request for animal crossing sign	Approved
250	676 Tillman Rd	7/12/05	Request upgrade to full signal	Not recommended
250	Int 250 & 616	5/27/05	Request left turn lane	Approved
631	At Rt 780	4/7/05	Request for signal at intersection	Not recommended
666	Allen Road	6/8/05	Request for posted speed limit	Signs installed 7/20/05
689	Birches Creek Rd	5/19/05	Speed review/posting of gravel road	Signs installed 7/20/05
1427	Northfield Rd	5/23/05	Request to install additional speed limit signs	
1427	Northfield Rd	5/5/05	Request for school bus & deaf child area	Signs installed 7/11/05
1436	Northfield Circle	5/5/05	Request for school bus & deaf child area	Signs installed 7/11/05

**Greene Complete June - July**

33	Main St & Shiloh	6/2/05	Request from Mayor	Crosswalk Sign
----	------------------	--------	--------------------	----------------


**Albemarle - Under review**

<b>Route</b>	<b>Location</b>	<b>Received</b>	<b>Issue description</b>	<b>Planned Action</b>
29	Int. 1105	7/11/05	Request to paint yellow lines in crossover	
614	Garth Road	6/27/05	Request for school bus stop ahead	
659	Woodburn Rd	7/20/05	Reduce speed from 35 to 24 MPH	
664	Markwood Road	6/27/05	Request for school bus stop ahead	
684	Half Mile Branch	6/27/05	Request for school bus stop ahead	
743	Earlsville Forest Dr	7/11/05	Request for 4 way stop at 743 & 660	
854	Carrsbrook Drive	6/27/05	Request to lower speed limit & post	Study by TE
1407	Int 1405	7/11/05	Request to upgrade two way stop to four way stop	

**Greene - Under review**

<b>Route</b>	<b>Location</b>	<b>Received</b>	<b>Issue description</b>	<b>Planned Action</b>
33Bus	Martha Jefferson	7/5/05	No parking in front of business for sight	
33Bus	Int 622	7/5/05	Repaint corner at int	
33	Int 622	7/1/05	Change signal from flashing to traffic light	
617	Fr 670 - 633	7/5/05	Request for centerline on road	
T649	Stanard Street	7/18/05	Reduce to one way for court expansion	Study by TE

**MAINTENANCE BUDGET**

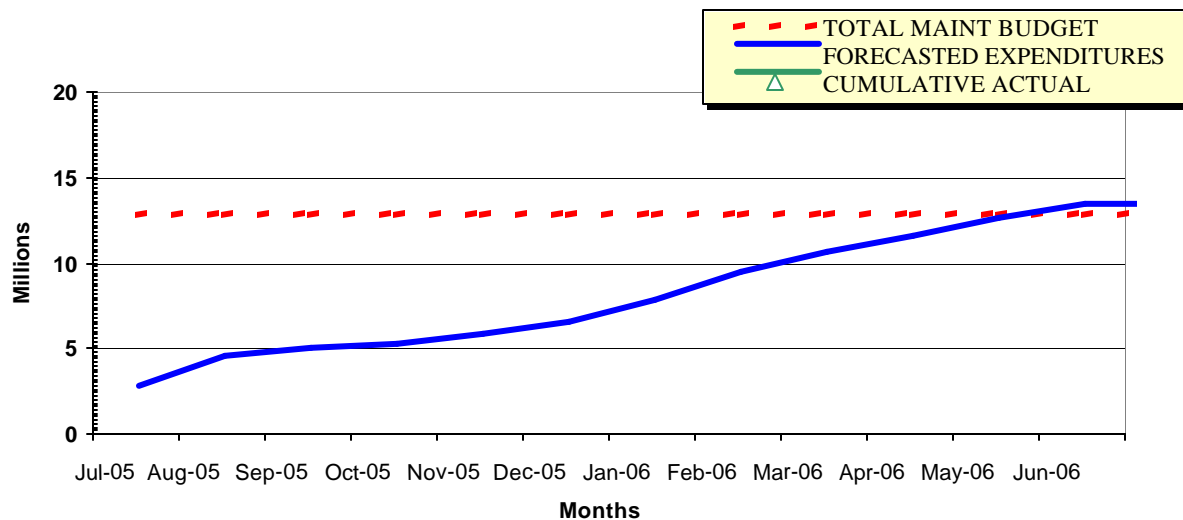

**PLANNED MAINTENANCE WORK – AUGUST 05**

- Complete all Secondary Mowing First Cycle
- Start second cycle of Secondary mowing
- Complete Rural Rustic Road project on Route 640 in Albemarle
- Finish Guardrail mowing on Route 20, Keene
- Patching Pot Holes on Secondary Rts. Various Locations
- Bridge Deck Replacement Rt. 628 Greene County
- Guardrail Mowing Rt. 250 from Mechum River Rt. 680 To Rt. 677
- Tree Contractor Working Cleaning up Trees from Storms Yancey Mills and Keene Areas
